Day Book



Leaving time from office/accomodation: 07.10	Leaving time from site: 16.00	
Time of arrival on site: 07.50	Time of arrival at office/accomodation: 16.50	
Staff on site:		
REW		
Weather: Overcast, mizzle clearing to sunny and warm		

Time	Occurrence
07.50	Arrived on site, shown where to park, commuting students carpark, recieved induction.
	The works this week entail the excavation of a storm drain linking in to existing services. Excavation is likely to be 0.5 m deep. Stratigraphy so far 0.25 m tarmac overlying concrete. Part 2 of the drain run penciled in for weds next week. Let SEC know.
10.00	Speak to AG and SDC, keep both updated on scope and timetable for works.
13.30	After lunch they start clearing up the broken tarmac, 13.45 ready to start digging
14.00	There is a pipe 0.56 m bgl at the s end of the trench, appears to come from one of the manholes that they are going to T in to. Otherwise strat is fairly straightforward 0.25 m tarmac overlying 0.10 my type 1 hardcore which overlies a mid reddish brown sandy clay with gravels. Rare modern inclusions are pressed in to the top but this appears to be the nat.
15.45	Excavation is finished. I have surveyed (GPS has to be returned). They have excavated to an average depth, tomorrow will excavate to required depth. Email AG and SDC to keep them appraised.

Last context number: 103		Last drawing number:
Last photograph number: 0028		Last survey number: 0022
Location of downloaded photographs	:	
Location of downloaded survey:	Ftp server	

Recorded by: REW		Date: 04/09/2019
	_	Continued on revers

T wesse archae	eology	T	Daybook	
Site Code	Site Name: Montefiore Boiler House, Southampton, Hampshire.			
Site sub-	division:			
1 4	···· • • • • • • • • • • • • • • • • •	1-4:	I I a suite su time a finanza atta.	
	ime from office/accomod	1ation: 07.10	Leaving time from site: 15.00	
	rrival on site: 08.00		Time of arrival at office/accomodation: 17.25 (via Soton Uni)	
Staff on s	ite:			
REW				
Weather:	\\/			
vveatrier.	Warm, dry, sunny			
Time	Occurrence			
08.00	Occurrence		N. F. de Cloude de Control	
06.00	catch up with daybook		n. No digging until 9 due to noise constraints so I sheet.	
08.55	_	-	over, they will be breaking concrete and moving	
	the tarmac spoil heap first so no digging for a while. Wait in the van.			
11.20	They are ready to start digging. It soon becomes clear that the clay and gravel deposits noted yesterday is the natural. There is a waterpipe cutting through, hence the dirty patch. Speak to AG and email him and SDC with photos demonstrating what I've seen. Persuade the groundworker's supervisor to let me machine clean the bit not being excavated to depth later to save a visit on Monday. They end up digging to their required depth as just easier for all!			
14.30	Finish excavating, D	arren (groundwork	s supervisor) thinks they will be ready to dig again	
	on Tues. Will get so	meone to ring him (07881 272618) to check on Monday. Pack up, leave	
	site at 3, go back to	WA via Soton Uni t	o collect the Tidgrove animal remains.	
Last cont	ext number: 105		Last drawing number: 101A (Rep sec)	
Last photograph number: 0049			Last survey number: NA	
Location	of downloaded photogra	phs: X:\PROJECTS	\222651\Photos\Temp	
Location	of downloaded survey:	NA		
Recorded by: REW			Date: 05/09/2019	

WA 20a

Site Code	Code: SOU1843 Site Name: Montefiore Boiler House, Southampton, H		
Sita sub.	division:		
Oite Sub-	division.		
Leaving t	ime from office/accomod	lation: 07.10	Leaving time from site: 14.00
Time of a	rrival on site: 08.20		Time of arrival at office/accomodation: 15.45
Staff on s	ite:		
REW			
Weather:	Cool, dry, sunshine and	d cloud	
	<u> </u>		
Time	Occurrence		
08.20	Arrived on Site, he	eavy traffic on the	e A34, I diverted around Winchester. Spoke to
	-	l backfilling, ther	have to break the tarmac. Sign in and wait in
	the van.		
10.30	Start digging. The excavation today comprises an L -shaped extension to TR1. Stratigraphically the sequence is similar to last time 0.5 m made ground overlying gravels. The made ground comprises pav slabs, yellow sand, concrete and a thin layer of grey sandy clay with modern inclusions. Much of the ground is cut by modern services, one manhole may date to 1995 (dated from a Tango can in the backt		
			· · · · · · · · · · · · · · · · · · ·
	1	•	ncilled in for Thursday. They are having a site then when the footings will be excavated. I keep
	SEC, AG and SDC		
14.00	Finished digging for th	e day. Return to W	A. M27 shut do forced to divert through Chandler's Ford
	and Romsey in heavy		·
Last cont	ext number:		Last drawing number:
Last phot	ograph number: 0069		Last survey number:
Location	of downloaded photogra	phs: arcserver	
Location	of downloaded survey:		
Recorded	by: REW		Date: 10/09/2019

wesse archae	x eology			Dayboo
Site Code: SOU1843 Site Name: Monte			fic	re Boiler House, Southampton, Hampshire.
Site sub-	division:			
Leaving ti	me from office/accomod	lation: 07.20	T	Leaving time from site: 12.40
Time of a	rrival on site: 08.00		1	Time of arrival at office/accomodation: 13.50
Staff on s	ite:			
REW				
Weather:	Cool, high cloud, dry			
Time	Occurrence			
08.00	Arrive on Site, no	ground workers, c	an	't dig until 9 anyway. Wait in van.
10.30	trial holes. Both de	emonstrate sustair		nis delivery and collection then we dig two ole truncation (both are located right next
	to the current build	ling)		
12.30	Excavation and recording is completed. Darren informs me that there will be no more excavation today. I thank him, pack up, sign out and return to WA.			
Last context number: 305			Last drawing number: Na	
-	ograph number: 0082			Last survey number: Na
	of downloaded photogra	phs: Arcserver		
Location	of downloaded survey:			
Recorded	by: REW			Date: 13/09/2019



LLI archaeology	rchaeology Dayboo			
Site Code: SOU1843	Site Name: Montefiore Boiler House, Southampton, Hampshire.			
Site sub-division:				
Leaving time from office/accomod	dation: _{7.40}	Leaving time from site: 13.00		
Time of arrival on site: 8.20		Time of arrival at office/accomodation: 14.30		
Staff on site:				
Piotr Orczewski				
Weather: Overcast				
Wedner Overcast				
Time Occurrence				
0.00	aducted and shown	n to site,however no work started before 9.		
Aiter airivai i got ii	iducted and snowi	i to site, nowever no work started before 9.		
9.00 Work started on a short sec	ction linking existing pipe with	n section watched by REW on 10.9.19 (tr3 I believe). The		
entirety of trench was dug t	hrough man made deposits	of shingle gravel .		
	The excavation stopped and I was told that section will be dug on Thursday (not			
Wednesday like prev		site manager, to confirm date via email) and		
	the wav back to office			
Look contové sousshor		Lost describe a propelation		
Last context number: Last photograph number:		Last drawing number: Last survey number:		
Location of downloaded photogra	nhs·	Last survey number.		
Location of downloaded survey:	P110.			
Recorded by: Po		Date: 16/09/2019		

Twessex Daybook				
Site Code: SOU1843				
Site sub-division:				
Leaving time from office/accomod	lation: o= o=	Logying time from site: as as		
Time of arrival on site: 08.00	1411011. 07.25	Leaving time from site: 09.50 Time of arrival at office/accomodation: 10.30		
Staff on site:		Time of arrival at office/accomodation. 10.30		
REW				
REVV				
Weather: Cool, dry, sunny				
Time Occurrence				
08.00 Arrive on Site and	Arrive on Site and sign in. Wait in the van as they can't dig until 9 am.			
He is surprised to se	Spot Darren, ask him if they will be ready to start digging at 9 or should I just wait in the van. He is surprised to see me as he had told PO no digging until Thursday, I explain that someone rang the office yesterday afternoon and requested our presence today.			
last visits). He did	Go to sign out, speak to Neil Fail (construction manager who was on leave for my last visits). He did ring the office and thinks they will be digging today. I wait in the office whilst he speaks to Darren.			
	Neil reappears, they are only breaking tarmac today so not required. EE is booked to cover tomorrow and Friday.			
09.30 Ring SEC, who re	Ring SEC, who requests I put all this in an email. Return home.			
Last context number:		Last drawing number:		
Last photograph number:		Last survey number:		
Location of downloaded photographs:				
Location of downloaded survey:				
Recorded by: REW		Date: 18/09/2019		

Site Code: SOU1843 Site Name: Monte		Site Name: M	ntefiore Boiler House, Southampton, Han	npshire.
Site sub-	-division:			
Leaving t	ime from office/accomo	odation: 7:15	Leaving time from site:	
Time of a	rrival on site: 8:45		Time of arrival at office/accomodation:	
Staff on s	site:		<u> </u>	
Eva Est	ela			
Wooth or:				
vveamer.	Sunny dry			
Time	Occurrence			
8:45	Arrived to site.an being inducted. 6 pits and 2 trenches need to be done between today and tomorrow. Next week a trench will be dug on Tuesday (tomorrow it will be confirmed.			
9:30	After clearing the area the digger starts pits Trench 4, Trench 5 and Trench 6, located in a row following W to E direction parallel to the North wall o the building. All of the ground, in any case they reached the geology. No archaeology found.			
13:30			pits 4, 5 and6. Pits 8 and 10 dug following N-S direction pits dug before, just made ground without reaching the	
	The made ground is very recordings done from the		en they dug trench 7 South side partially collapsed. All the collapsing sides.	
16:00	Leaving site			
17:00	Arriving to the off	ice		
Last cont	ext number:		Last drawing number:	
Last photograph number:			Last survey number:	
	of downloaded photogr	•		
Location	of downloaded survey:			



W archaeology				
Site Code	s: SOU1843	Site Name: Montefiore Boiler House, Southampton, Hampshire.		
Site sub-division:				
Leaving ti	me from office/accomod	lation: _{7:05}	Leaving time from site: 12:00	
Time of ar	rrival on site: 8:00		Time of arrival at office/accomodation:	
Staff on si	ite:			
Eva Est	ela			
Weather:	Cuppy and day			
VVCdtrici.,	Sunny and dry			
Time	Occurrence			
8:00	+	onfirmed that next	week and archeologist will be needed next	
	week but not on M		wook and dronoslogist will be needed next	
9:30	Pit 9 dug between	pit 10 and pit 8.		
	-			
12:00	Leaving site			
	•			
Last context number: Last drawing number:		Last drawing number:		
Last photo	ograph number:		Last survey number:	
	of downloaded photogra	phs:		
Location of	of downloaded survey:			
Recorded	by: EE		Date: 20/09/2019	
			Continued on reverse	

Wesse	ex eology		Daybook
	e: SOU1843	Site Name: Monte	fiore Boiler House, Southampton, Hampshire.
Site sub	-division:		
Leaving t	ime from office/accomod	dation: 0700	Leaving time from site: 1500
	arrival on site: 0750	Janon: 0700	Time of arrival at office/accomodation: 1600
Staff on s			Time of all the actions of action 1990
Peter C			
Weather:			
Time	Occurrence		
0750	Occurrence		
0730	9am. Then they w	•	nd site manager. No work allowed on site until tings.
0900			
0900	wait for structural eng		of existing buildings footings means they need to ntinuing.
1100	Start digging drain	nage while waiting	for engineer.
1430			to put pipe in and backfill before continuing
	started.	so no more diggin	g today. Photo taken and trench sheet
1500			
1300	Leave site		
1600	Arrive at office.		
	,		
Last cont	ext number:		Last drawing number:
-	tograph number:		Last survey number:
	of downloaded photogra	iphs:	
Location	of downloaded survey:		
Recorded	t by: Do		Date: 24/00/2010
1.ecolue(4 Dy. FC		Date: 24/09/2019



Wesse archae	eology		Daybook				
Site Code	iore Boiler House, Southampton, Hampshire.						
Site sub-	-division:						
L eaving t	ime from office/accomod	lation: 0745	Leaving time from site: 1300				
	rrival on site: 0820	1011.0715	Time of arrival at office/accomodation: 1430				
Staff on s			Time of arrival at office/accomodation. 1430				
Peter C							
1 0101 0	<u>арро</u>						
Weather:							
	T						
Time	Occurrence						
0820	Arrive on site and	wait for work to sta	ırt.				
0900	Ctart diagrica duair	ana continuation t	imana va atanda v (trd 4)				
	Start digging drain	age, continuation i	rom yesterday (tr11).				
1230	Finished diagina s	o survey trench an	d finish recording.				
1300	No more excavation	on todsay just back	filling, leave site.				
1415	Arrive at office, up	date daybook and	timesheet etc.				
Last cont	ext number:		Last drawing number:				
Last phot	ograph number:		Last survey number:				
Location	of downloaded photogra	phs:					
Location	of downloaded survey:						
Recorded	by: Pc		Date: 26/09/2019				
			Continued on revers				

Site Code	e: SOU1843 	Site Name: Mon	tefic	ore Boiler House, Southampton, Hampshire.					
### Daybook Site Code: SOU1843 Site Name: Montefiore Boiler House, Southampton, Hampshire.									
		lation: ₀₇₄₅	-						
Time of a	rrival on site: 0855			Time of arrival at office/accomodation:					
Staff on s	site:								
Peter C	apps								
Weather									
- VVCatrior.									
	Occurrence								
		diaging until afte	or to	a break when they will strip an area for					
	I		יו נכ	a bleak when they will strip an area lor					
		<u> </u>							
1130	No ore space for s	poil and issues	with	granting it removed from site. Site manager					
			7710						
1320	No muck away un	til tomorrow so n	o m	ore digging today.					
	,			33 3 3					
1335	Leave site.								
				-					
				Last survey number:					
		pns:							
Location	oi downioaded survey:								
D	l le D		٦	D-4- 00/00/0043					
Recorded	a by: Pc			Date: 26/09/2019					



W archae	eology			Daybook			
Site Code	s: SOU1843	Site Name: Montef	efiore Boiler House, Southampton, Hampshire.				
Site sub-	division:						
Leaving ti	me from office/accomod	ation: 7.30	Leaving time from site: 14.30				
Time of a	rrival on site: 8.10		Time of arrival at office/accomodation	n:			
Staff on s	ite:						
Piotr Or	czewski						
Weather:							
Time	Occurrence						
8.10	On site,nothing ha	ppens till 9.					
12.00	Start of excavation	of footing trench (tr12).				
13.00	I inform Alex abou	t it,he says he'll try	to get Ingrid here on Monday. N	lo backfilling			
	till then.	-					
13.30							
Last conte	ext number:		Last drawing number:				
Last phot	ograph number:		Last survey number:				
Location	of downloaded photogra	phs:					
Location	of downloaded survey:						
Recorded	l by:		Date:				
				Continued on reverse			

Wesse archae	eology			Daybook			
Site Code	e: SOU1843	Site Name: Monte	efic	ore Boiler House, Southampton, Hampshire.			
Site sub-	-division:						
Leaving t	ime from office/accomoc	lation: ₇₃₀	T	Leaving time from site: 1500			
Time of a	rrival on site: 840			Time of arrival at office/accomodation: 1615			
Staff on s	site:						
Td							
Weather:	Dry						
· · · · · · · · · · · · · · · · · · ·	<u> </u>						
Time	Occurrence						
0840	Arrive on site park	van where instru	ıcte	ed (so I don't get a ticket)			
	7 trive on site, part	C van where mand	iot	sa (so i doirt got a tioket)			
0845	Sign in and have s	short induction witl	h s	site manager.			
	_						
0908				. Discuss background of project and			
	methods for today	. Ingrid P. Confirm	nec	d visit today for 2pm.			
0915	I give driver quick brief on what	I need. We start machining.					
0313	Continue digging until 10am. Du	uring this time I take working sl	hots	of what is disturbed and made ground including foul drainage (probably excavat			
	concrete storm drain. Cannot see Pecker is required to break thro	ee any archaeology, ground is ugh concrete drain.	pret	ty well turned over with frogged bricks and concrete appearing at lower depths o			
1000	Break.						
	Droun.						
1045				tart scraping down to finished level. Possibly			
				y loose. Some frags if tarmac in lower parts of ed I record trench - trench sheet numbered as			
	30 for today's date. N	ot sure what last nun	nbe	er used is but can't be more than 30.			
<u> </u>			_				
	ext number:			Last drawing number:			
-	ograph number: of downloaded photogra	nhe:		Last survey number:			
	of downloaded survey:	γ.10.					
Recorded	 d by: Td]	Date: 30/09/2019			

Trench Records




Site Sub	-divisior	ո։				Trench	no: 1					
Machine	ed 🖊 H	and dug	Len	gth (m):		Width (m)	: 0.85	Thi	ckness/de	pth <i>(m)</i> : ().60	
X co-ord	d:			Y co-or	Y co-ord: Ground leve							
Context number	Cont type		Fill of/ filled with	Interpret	tative cate	gory/descrip	otion			Depth from	om ground (m)	
101	Laye	er		Made Gr	ound. Tarı	тас.				0.00	- 0.25	
102	Laye	er		Made Ground	d. Type 1 hard	core, compacte	d with a clear u	ındulating horiz	on with (103)	0.25 - 0.58		
103	Laye	er		Natural.	Mid reddisl	h brown sar	ndy clay wi	th abundar	nt gravels.	0.3	36 +	
104	Cut			Modern Service. m deep.	Gas pipe trench se	en obliquely within the	e trench, aligned E-	W, 3.1 m wide, base	e not seen at 0.60	0.25 -	0.60 +	
105	Fill			Deliberate backfill. stamped where vis	Redeposited natura sible) and tarmac. Bl	ll sandy clay and grave ue plastic marker tape	els with fragments of C lay above the pipe, e	CBM (machine made xcavation ceased on	bricks, frogged and finding the tape.	0.25 -	0.60 +	
106	Cut			Modern Serv	vice. Waste wa	ater pipe, aligne	d NE - SW, ful	ll extent of the	cut not seen.	0.17	- 0.56	
107	Fill			Deliberat	e backfill.	Concrete.				0.17 -	0.41 +	
108	Fill			Deliberate backfil surrounding the v	II. Mid-grey sandy o vaste water pipe.	lay with sparse grave	l inclusions. Modern	inclusions of wood,	CBM and plastic	0.41	- 0.56	
Plans:				Section	s:			Photog	raphs:			
								0034 -	36			
Context:	Pottery	Animal bone	Worked flint	Burnt flint	Fired clay	СВМ	Slag	Metal object	Marine shell	Stone	Other (specify)	
Object n	os:	<u>I</u>				Sample	nos:	1		<u> </u>		
Recorded	v. DE/V	ı	Det	٥٠.		Checked	l hv:			Date:		
Recorded by: REW Date:						Checked	i by.				and on reverse	




Site Code: SOU1843	Site Name:	Montefiore Boiler House,	Southampto	n. Hampshire.	
110 10 10 10		Montonoro Bonor Franco,	Coathampto	n, maniponico.	

Site Sub-division:							Trench	no: 2							
Machine	Machined Hand dug Length (m				th (m): 2.	90	Width (m)	: 0.70		Thic	kness/de	pth (m): 1.12			
X co-ord	:					Y co-ord	l :			Gro	ound	level:			
Context number	Co typ	ntext e		l of/ ed with	1	Interpreta	ative categ	gory/descrip	otion	•			Depth from ground surface (m)		
201	Lay	er/				Topsoil. Dark of Turf covered w			A gravels. Loose	e with a	distinct	horizon with 2	0.00	- 0.12	
202	Lay	er/				Subsoil. Mid	brown sandy	clay with rare	flint gravels. (Overlies	s 204 a	nd 205.	0.12 - 0.38		
203	Cut		FW (2	204), (205),	(206).	Construction	cut. Cut for o	concrete slab.	Not visible in p	plan, dii	mensio	ns unknown.	0.38	- 0.93	
204	Fill		F	O [20	3]	Delibera	ate back	fill. Mode	ern concr	ete s	slab.		0.38	- 0.70	
205	Fill		F	O [20	3]	Redeposited	natural. Dark	reddish brow	n sandy clay v	with rare	e brick	inclusions.	0.38	-0.70	
206	Fill		F	O [20	3]	Delibera	ate back	fill. Grave	els				0.70	- 0.90	
207	Lay	er/er				Natural. Mid reddish brown sandy clay with abundant gravels					0.9	0 +			
Plans:						Sections:				Photographs:					
										007	74, 0	077, 00	78		
Context:	Pottery	Anim		Worke flint		Burnt flint	Fired clay	СВМ	Slag	Me	etal ect	Marine shell	Stone	Other (specify)	
							,			,				(=	
Object no	os:							Sample	nos:						
Recorded by	: RF\	Λ/			Date:	13/09/	19	Checked	l by:				Date:		
	Recorded by: REW Date					10/00/									









Notes:									
Small trial hole located next to the extant									
building. Natural truncated to 0.90 m below ground level.									
Project specific operational fields									
No archaeology: Recording completed: 13/09/19									
Date Surveyed: Signed off:									
Photos date: 13/09/19 Backfilled: 13/09/19									
Date of decision not to excavate as planned:									



Site Sub	-division	:					Trench no: 3						
Machine	d 🖊 Ha	and du	g	Len	gth <i>(m)</i> : 1 .	60	Width (m):	0.80	Thi	ckness/de	epth (m): 1.00		
X co-ord:						d:			Ground	level:			
Context number	Cont type	ext	Fill fille	of/ ed with	Interpret	ative categ	jory/descrip	tion		om ground (m)			
301	Laye	r			Topsoil.	Mid gre	y brown	loam			0.00 - 0.20		
302	Laye	r			Made ground	d. Yellow san	d and gravels v	with rare brick	inclusions.		0.20 - 0.35		
303	Cut		FW	(304), (305	Constru	ction cu	t. For mo	dern for	footing		0.35	- 0.90	
304	Fill		F	C [303]	Delibera	ate back	fill. Mode	rn concr	ete slab		0.35	- 0.90	
305	Fill		F	C [303]	Redepos	ited natu	ral. Dark g	reyish bro	own sandy	/ clay.	0.35	- 0.90	
Plans:					Sections	s:			Photographs:				
									0075, 0	0076, 00	79 -81		
Context:	Pottery	Anima		Worked flint	Burnt flint	Fired clay	СВМ	Slag	Metal object	Marine shell	Stone	Other (specify)	
		DOTTE	7		IIIIC	Clay			Object	SHEII		(Specify)	
Object no	os:						Sample	nos:					
Recorded by	RFW			Dat	≕ 13/09/°	19	Checked	by:			Date:		
Recorded by: REW Date: 13					13/00/	. •		•					



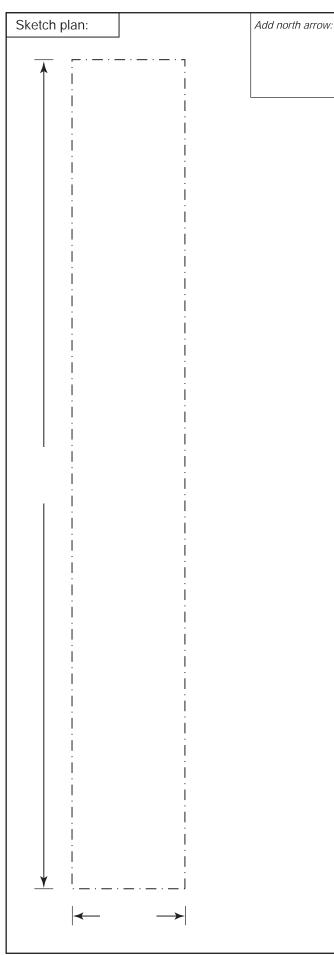




Notes:										
Small trial hole next to the extant building. Natural truncated to 1 m + below ground										
level.										
Project specific operational fields										
No archaeology: Recording completed: 13/09/19										
Date Surveyed: Signed off:										
Photos date: 13/09/19 Backfilled: 13/09/19										
Date of decision not to excavate as planned:										




Site Code: SOU1843	Site Name:	Montefiore Boiler House	, Southampton, Hampshire.	
1100 100 100 100 100 100 100 100 100 10		Wichitolici C Bollot i lodoc	, Codularipton, Harriponic.	

Site Sub	-divisi	on:					Trench no: 4						
Machine	ed 🗸	Hand du	g	Leng	th <i>(m)</i> : 1 .	40	Width <i>(m)</i>	: 1.10	Thic	ckness/de	oth <i>(m)</i> : C).70	
X co-ord	l:				Y co-ord	l:			Ground	level:			
Context number	Co typ	ontext be	Fill fille	of/ ed with	Interpreta	ative categ	gory/description				Depth fro	om ground (m)	
401	La	yer			Modern made	ground. Light	reddish brown sandy gravels with a very loose compaction.				0.00	- 0.30	
402	La	yer			Modern made grou -20mm.	ınd. Mid yellowish t	orown clayish sand with a loose compaction. Abundant gravels +50% 100 mm				0.30+		
Plans:					Sections	3:			Photogr	aphs:			
									082, 08	33			
Context:	Pottery	Anim		Worked flint	Burnt flint	Fired	СВМ	Slag	Metal	Marine shell	Stone	Other	
		DOTTE	3	- IIIIIL	IIIII	clay			object	SHEII		(specify)	
Object nos:						Sample nos:							
Recorded by: EE Date: 19/09/19						19	Checked	l by:			Date:		
											Continu	ed on reverse	







Notes:									
Pit excavated through 2 layers of modern made ground, which also were disturbed at the North side of the pit by the cut of a service. The geology was not reached.									
No archaeology									
Gps0001 to GPS009									
Project specific operational fields									
No archaeology: Recording completed:									
Date Surveyed: Signed off:									
Photos date: Backfilled:									
Date of decision not to excavate as planned:									



Site Sub	-divisi	on:					Trench no: 5					
Machine	ed 🗸	Hand du	ıg	Len	gth (m): 1.	60	Width (m)	: 1.30	Thic	ckness/de _l	oth <i>(m)</i> : C).75
X co-ord	:			'	Y co-ord	d:			Ground	level:		
Context number	Co typ	ontext pe	Fill fille	l of/ ed with	Interpreta	ative categ	gory/description				Depth fro	om ground (m)
501	La	yer			Modern made	ground. Light	reddish brown	sandy gravels w	e compaction.	0.00	- 0.30	
502	La	yer			Modern made grou -20mm. In section	ınd. Mid yellowish l fragments of mode	brown clayish sand with a loose compaction. Abundant gravels +50% 100 mm rn bricks and tarmac observed.				0.3	30+
									Ι			
Plans:					Sections	S: 			Photogr	aphs:		
									084, 08	35		
Context:	Pottery	, Anim		Worked flint	Burnt flint	Fired clay	СВМ	Slag	Metal object	Marine shell	Stone	Other (specify)
										211211		(=====,)
Object no	os:						Sample	nos:				
1												
Recorded by	/: EE			Date	19/09/	19	Checked	l by:			Date:	
									Ī	Continu	ed on reverse	



Sketch plan:		Add north arrow:	Sketch section:
	•		
 	-·-·-· ₁		
	<u> </u> 		
	 - 		
	 - 		
	:		
i	:		
i	:		
i	: 		
i	:		
i	i		
i	i		
i	i		
	i		
	į		
	i		
	i		
	į		
ļ :	į		
	<u> </u>		Notes:
	<u> </u> :		Pit excavated through 2 layers of modern
	<u> </u>		made ground. At the base of the pit there
	<u> </u> -		was a blue plastic related to a buried service.
	<u> </u> 		Service.
	<u> </u> 		No archaeology Geology not reached.
	 		Geology not reached.
;	: 		GPS 010 to 014
	: İ		
ļį	i		
ļ ļ	į		
	į		
	<u> </u>		
	<u> </u> :		
	! !		Project specific operational fields
	i		No archaeology: Recording completed:
<u> </u>	. _ . _ . _ İ		Date Surveyed: Signed off:
 ←			Photos date: Backfilled:
'			Date of decision not to excavate as planned:



Site Sub-division:							Trench no: 6					
Machine	ed 🗸 H	Hand du	ıg	Len	gth (m): 1.	50	Width (m)	: 1.30	Thi	ckness/de	oth <i>(m)</i> : C	0.80
X co-ord	l:			'	Y co-ord	d:			Ground	level:		
Context number	Cor	ntext	Fill fille	of/ ed with	Interpret	ative cate	gory/descrip	otion			Depth fro	om ground (m)
601	Lay	er			Modern mad	e ground. Mi	d yellow sand	laid of below t	he tarmac to I	evel the area.	0.00	- 0.15
602	Lay	er			Modern mad	e ground. Liç	ght reddish bro	wn sandy gra	ry loose comp			
603	Lay	er			Modern made gro -20mm. In section	und. Mid yellowish was possible see	brown clayish sand fragments of modern	with a loose compac bricks and tarmac.	tion. Abundant grav	els +50% 100 mm		
Plans:					Sections	S:			Photog	raphs:		
									084, 0	85		
Context:	Pottery	Anim		Worked flint	Burnt flint	Fired clay	СВМ	Slag	Metal object	Marine shell	Stone	Other (specify)
						-						
Object no	os:						Sample nos:					
Recorded by: EE Date: 19/09/19						19	Checked	l by:			Date:	
_ 											Continu	led on reverse




Sketch plan:	Add north arrow:	Sketch section:
<u> </u>		
l li i		
!		
; ;		
!		
! !		
į į		
į į		Notes:
, i		
		Pit excavated through 3 lay
		made ground.
		Coology not reached
		Geology not reached.
		No archaeology
!		
!		
į į		
		Project specific operational fields
! : :		No archaeology: Recording of
<u> </u>		Date Surveyed: S
 ← →		Photos date:
		Date of decision not to excavate as plann



Site Code: SOU1843	Site Name:	Montefiore Boiler House	Southampton, Hampshire.	
	Oito Haillo.	With the policy induse,	, oouthampton, nampanire.	

Site Sub-division:								Trench no: 7					
Machine	ed 🗸 l	Hand du	ıg	$\exists \lceil$	Leng	th (m): 4.	20	Width (m)	: 0.60	Thi	ckness/de _l	oth <i>(m)</i> : C	0.80
X co-orc	l:					Y co-ord	d:			Ground	l level:		
Context number	Cor	ntext e	Fil fille	l of/ ed w	vith	Interpreta	ative cate	gory/descri	ption			Depth fro	om ground (m)
701	Lay	er				Modern mad	e ground. Lig	ght reddish bro	wn sandy gra	ry loose comp	0.00	- 0.20	
702	Lay	er				Modern made gro -20mm. In section	und. Mid yellowish was possible see	brown clayish sand fragments of modern	with a loose compac bricks and tarmac.	vels +50% 100 mm	0.2	20 +	
Plans:	<u> </u>					Sections	S:			Photog	raphs:		
										089 to	091		
Context:	Pottery	Anim			orked lint	Burnt flint	Fired clay	СВМ	Slag	Metal object	Marine shell	Stone	Other (specify)
		DOTA				IIIIIC	olay			Object	311011		(эрсспу)
Object n	os:							Sample	nos:				
						10]						
Recorded by: EE Date: 19/09/						19/09/	19	Checked	з ру:			Date:	led on reverse



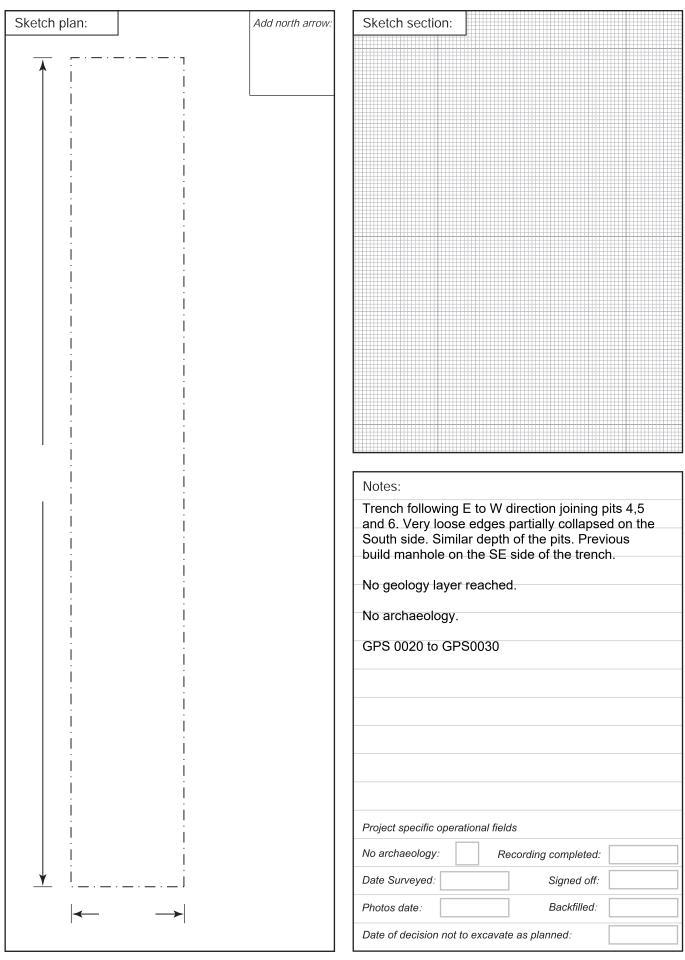



Site Code: SOU1843	Site Name:	Montefiore Boiler House	Southampton, Hampshire.	
0.10 00 10 10	0110 11011101	Widthchiold Dollar House,		

Site Sub	-divisio	ո։					Trench no: 8						
Machine	d 🖊 H	and du	g	Leng	th (m): 1.	00	Width (m)	: 1.40	Thi	Thickness/depth (m): 0.60			
X co-ord	:				Y co-ord	l:			Ground	l level:			
Context number	Con- type		Fill fille	l of/ ed with	Interpreta	ative cate	gory/description				Depth fro	om ground (m)	
801	Laye	er			Modern mad	e ground. Lig	ght reddish bro	wn sandy gra	ry loose comp	0.00 - 0.30			
802	Laye	er			Modern made gro -20mm. In section	und. Mid yellowish was possible see	brown clayish sand of fragments of modern	with a loose compac bricks and tarmac.	ction. Abundant grav	0.30 - 0.50			
803	Laye	r			Modern made the plastic pipe		ellow gravels. Gr	avels laid off to	locate a service	e. It is possible to	0.5	0 +	
Plans:					Sections: Phot				Photog	raphs:			
									094 , 0	95			
Context:	Pottery	Anima bone		Worked flint	Burnt flint	Fired clay	СВМ	Slag	Metal object	Marine shell	Stone	Other (specify)	
			\top										
Object no	os:						Sample nos:						
Recorded by: EE Date: 19/09/19						Checked	by:			Date:			
19/09/19									-	Continu	ed on reverse		




Sketch plan:	Add north arrow:	Sketch section:
<u> </u>		
i i		
i		
i i		
i i		
i i		
i i		
i i		
i i		
i i		
i i		
' i ;		
i i		Notes:
i i		
i i		Pit excavated at the South side of pit 4 through 3 layers of modern made ground. Bottom layer (803) have a plastic pipe following W-E direction.
i i		have a plastic pipe following W-E direction.
i i		No geology reached.
i i		No archaeology.
i l		GPS 0033 to GPS0037
i i		
i i		
i i		
i i		
i i		
į į		
į į		
į į		
		Project specific operational fields
		No archaeology: Recording completed:
<u> </u>		Date Surveyed: Signed off:
 ← →		Photos date: Backfilled:
· · · · · ·		Date of decision not to excavate as planned:



Site Code: SOU1843	Site Name:	Montefiore Boiler House	Southampton, Hampshire.	
0.10 00 10 10	0110 11011101	Widthchiold Dollar House,		

Site Sub-division:								Trench	Trench no: 9					
Machine	ed 🗸	Hand du	ıg		Leng	th (m): 1.	60	Width (m)	: 1.30	Thic	ckness/de	epth (m): 0.80		
X co-ord:					Y co-ord	l:			Ground	level:				
Context Context Fill of/ number type filled with					Interpreta	ative cate	gory/descrip	otion			Depth from ground surface (m)			
901 Layer					Garden soil. N	/lid brown loa	ım with a very l	oose compaction	on and abunda	int tree roots.	0.00	- 0.30		
902 Layer					Modern made gro -20mm. In section	und. Mid yellowish was possible see	brown clayish sand fragments of modern	with a loose compac bricks and tarmac.	tion. Abundant grav	els +50% 100 mm	0.3	0 +		
Plans:					Sections	3:			Photogi	graphs: D 102 Marine shell Stone Other (specify)				
									100 to	102				
										700 10				
Context:	Pottery	Anim			orked lint	Burnt flint	Fired clay	СВМ	Slag	Metal object		Stone		
		5011					oldy			Object	Orion		(opeony)	
			\dashv											
			\dashv											
Object ne	os:							Sample	nos:					
Pocorded by: FF Deter 20/00/40						Checked	I by:			Date:				
Recorded by: EE Date: 20/09/19					SHOOKE	· J ·				ed on reverse				



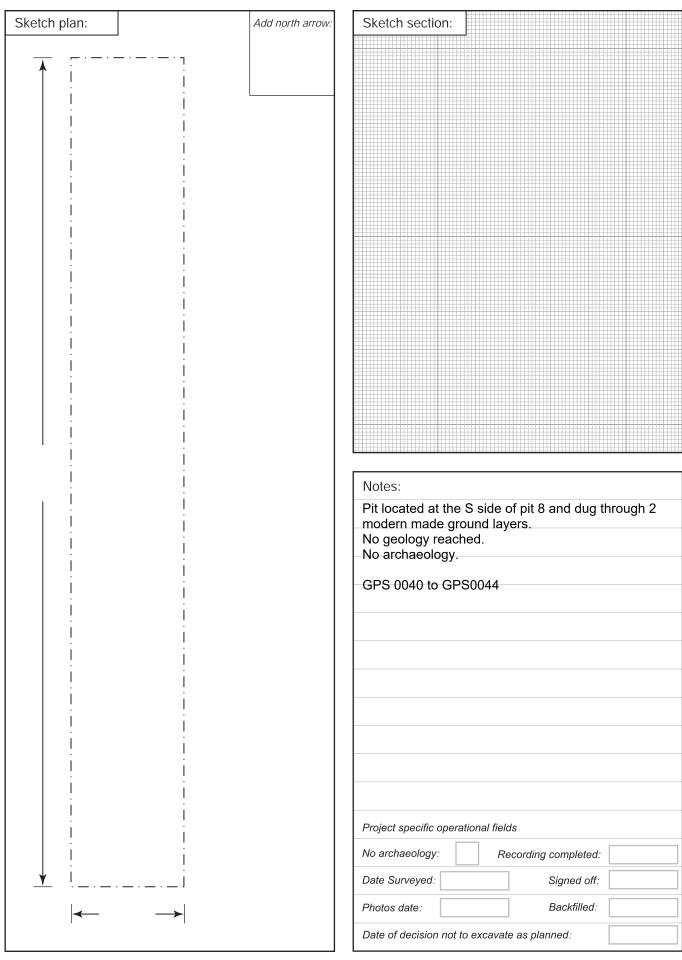



Site Code: SOU1843	Site Name:	Montefiore Boiler House	Southampton, Hampshire.	
0.10 00 10 10	0110 11011101	Widthchiold Dollar House,	, Codinarripion, Harripsinic.	

Site Sub	-divisio	n:				Trench	no: 10							
Machine	ed 🖊 H	and du	g	Leng	th (m): 1.	70	Width (m)	: 1.30	Thickness/depth (m): 1.00					
X co-ord	l:				Y co-orc	l:			Ground	level:				
Context number	Con type		Fill fille	of/ ed with	Interpreta	ative cateo	gory/descrip	otion	'		Depth fro	om ground (m)		
1001 Layer				Modern made	e ground. Lig	ht reddish bro	wn sandy grav	vels with a ver	y loose comp		- 0.40			
1002	Laye	er			Modern made gro	und. Mid yellowish was possible see fi	brown clayish sand v ragments of modern	with a loose compac bricks and tarmac.	tion. Abundant grave	els +50% 100 mm	0.4	ł0+		
Plans:					Sections	 3:			Photogr	raphs:				
										096 to 099				
									096 10	099				
)A/	D 1	E: 1								
Context:	Pottery	Anima bone		Worked flint	Burnt flint	Fired clay	СВМ	Slag	Metal object	Marine shell	Stone	Other (specify)		
Object no	os:	1					Sample	nos:	1			<u>'</u>		
						Charles	l by:			Data				
Recorded by	y. C			Dale	20/09/1	19	Checked	by.		Г	Date:	ed on reverse		




Sketch plan:	Add north arrow:	Sketch section:
<u> </u>		
i		
i		
i		
i		
l i		
i i		
i		
i i		
i i		
i i		
! i		
!		Notes:
		Pit located at the S side of pit 9. The South and the West edges of the pit wer corner of the North wall of the building, in the section of that sides it is possible.
!		foundations.
!		No geology reached
		No archaeology.
		GPS 0045 and GPS0046
i		
i i		
i		
i i		
i i		
i !		
		Project specific operational fields
↓		No archaeology: Recording completed: Date Surveyed: Signed off:
		Photos date: Backfilled:
→		
		Date of decision not to excavate as planned:



Site Sub-division:								Trench no: 11					
Machine	ed 🗸 F	land du	g	Len	gth (m): 1 2	2.00	Width (m)	: 0.50	Thi	ckness/de _l	epth (m): 0.70		
X co-ord:					Y co-ord	d:			Ground	level:			
Context number Context type Fill of/ filled with					Interpret	ative cate	gory/descrip	otion			Depth fro	om ground (m)	
1101 Layer			Modern s	urface. Blo	ockwork and	d associate	ed sand set	ting.	0.00	- 0.30			
1102 Layer			Made ground	d. Imported s	tone and grave	els. Greyish re	eddish brown.		0.	30			
1103	Laye	er			Made ground. sherds of plas	Reddish brow tic within. Prob	n poorly sorted s ably redposited i	ands and travel natural from nea	s. Brick and tarr arby, possibly fro	mac fragments a om within site it':	0.30 -	0.70+	
									T				
Plans:					Sections	S:			Photog	aphs:			
						102-122							
Context:	Pottery	Anim		Worked flint	Burnt flint	Fired clay	СВМ	Slag	Metal object		Stone		
						-							
Object no	os:						Sample	nos:	I			l	
Recorded by	y: Pc			Date	e:		Checked	by:		ı	Date:		
										Continu	ed on reverse		



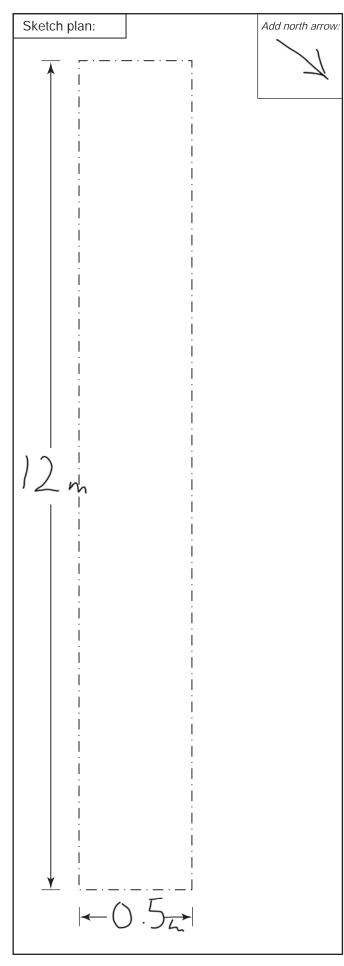

61 1 1 1		
Sketch section:		

Notes:								
Trench dug for drainage								
Project specific operational fields								
No archaeology: Recording completed:								
Date Surveyed: Signed off:								
Photos date: Backfilled:								
Date of decision not to excavate as planned:								



Site Code: SOU1843	Site Name:	Montefiore Boiler House.	Southampton, Hampshire,	


Site Sub	-divisi	on:					Trench	no: 12				
Machine	ed 🗸	Hand du	g	Ler	gth (m): 5	.00	Width (m)	: 1.30	Thic	ckness/de	pth <i>(m)</i> : C	0.60
X co-ord	l:			'	Y co-ore	d:			Ground	level:		
Context Context Fill of/ number type filled with			Interpret	ative cate	gory/descrip	otion	•		Depth fro surface (om ground (m)		
1201					Made Gro	und. Thin la	yer of made	ground und	der previous	building.	0.00	- 0.05
1202					Natural. S	andy grave	els. Mid brov	nish yellow	v. Sub angu	lar, 1-5cm.	0.05	- 0.60
Di					0 4:							
Plans:					Sections: Photographs:							
Context:	Pottery	Anim bone		Worked flint	Burnt flint	Fired clay	СВМ	Slag	Metal object	Marine shell	Stone	Other (specify)
Object no	os:						Sample	nos:				
Recorded by	y: Po			Da	e: 27/09/	19	Checked	by:			Date:	




Site Code: SOU1843 Site Name: Montefiore Boiler House, Southampton, Hampshire.

Site Sub-division:							Trench	no: 30					
Machine	d 🗸	Hand d	ug		Leng	th (m): 8.	00	Width (m)	: 1.30	Th	nickness/de _l	pth (m): 1.00	
X co-ord						Y co-ord: Ground level:							
Context number		ontext pe		ill of. led		Interpreta	Interpretative category/description					Depth fro	om ground (m)
3001	La	yer				Paving stone	s - Current su	urface of yard/	footpath. Macl	hine cut, sq	uare shape. 0.1	0-0	0.10
3002	La	ayer				Foundati	on - Yello	wish sand	base for	stone sl	abs.	0.10	-0.20
3003	La	ıyer				Deliberate du	ımp - layer of	grey type 1 s	tone, presuma	ıbly used to	level ground su	0.30	-0.60
3004	Fil			30	05	Concret	e storm	drain.				0.60	-0.95
3005	Cı	ut		30	04	Modern cut for not visible in se		rain ran directly	through centre of	of trench and	now it's removed	0.60	-0.95
3006	La	yer				Disturbed grou			to layer below b	out probably o	disturbed during	0.60	- 0.95
3007	La	yer				Gravel - possibly natur Rounded pebbles and size and in rare quant	more angular stones. (soft/loose and may also l Coast supported (very lit	oe disturbed. Mid brown le soil). Also contains so	colour, fairly well so me black clinker(ish	rted. Various shapes incl.) components around 0.05 i	9.0	95+
3008	Fil	II		30	09	New fou	ıl drain.					0 -0	0.95
3009	Сι	ut		30	80	Cut for a	above.					0-0).95
3010 Layer										components of sr rrent ground level.			
3011	La	ayer				Made ground - brownish grey layer containing modern rubble such as bricks and							
3012	La	ayer				Dark grey/black layer, fairly compact containing elements from above and below.							
Plans:						Sections: Photographs:							
Reverse)					Revers	e			142 -	166		
Context:	Pottery	Ani y bo			orked flint	Burnt flint	Fired clay	СВМ	Slag	Metal object	Marine shell	Stone	Other (specify)
							<u> </u>			0.0,000	0.110.11		(0,000)
Object no	s:							Sample	nos:				
Recorded by	· T~				Data	20/00/	10	Chooked	by:			Date:	
necorded by	· I a				Date	30/09/	19	Checked	by.			Date:	



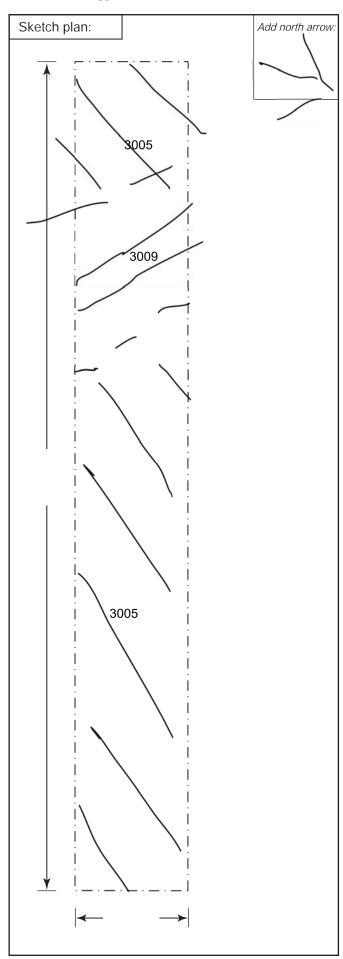

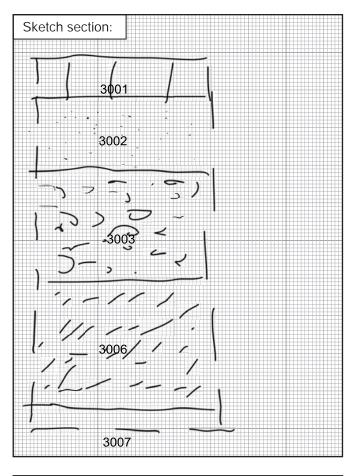


Notes:							
3009 looks to have been cut from surface.							
3005 is stratigraphically below 3003.							
Note trench number refers to today's date 30/09/2019							
Project specific operational fields							
No archaeology: Recording completed: 30/09/19							
Date Surveyed: 30/09/19 Signed off: 30/09/19							
Photos date: 30/09/19 Backfilled:							
Date of decision not to excavate as planned:							

Graphic Register

WA 8 Sheet Dwg no Co-ords Checked on dwg? by Site Sub-div Description Sect on Dwg **田archaeology** SOU 1843 Site Code: 222651 Initials & date size plan no scale A4 SKETCH PLAN 30/9/19 BAME (REP SEC 1 1710 SKETCU REP SEC 2 SKETCH 110 Sherch PLAN OF WORKS 19/9/19-20/9/19 Site Name: MUNTEFIORE SOTON HANTS © Wessex Archaeology 2015

Graphics Register

Site Drawings

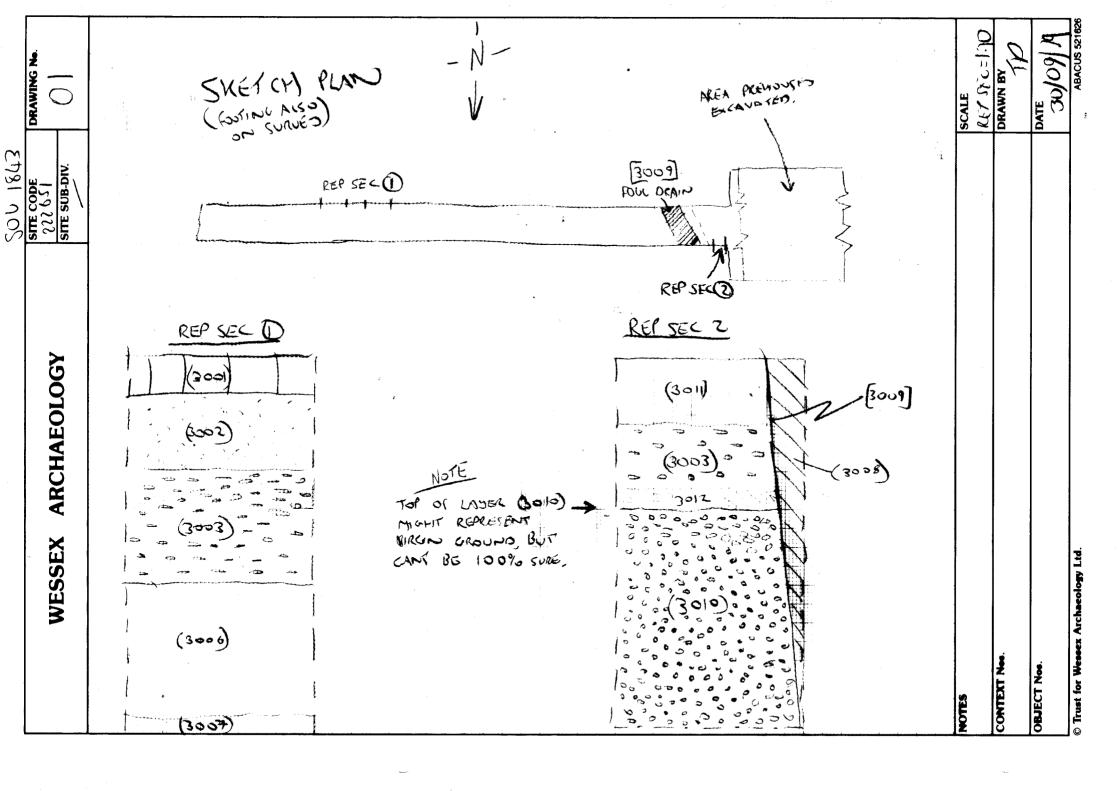

wessex archaeology 500 1843

Site Code:

Site Name:

Site sub-division:		Continuation of record no:
Continuation of field:	SKETCH OF 19/09/19-	THE WORKS CARRIED OUT 20/09/19
		
	BUILDING	
	S	STREST

Photographic Record

⊞wessex archaeology

Site Code: 7222651 / SOU Site Name: MONTEFIONE BOILER HOUSE SOUT YAMPTON, LAWTS

PO/PS:	REW	Camera no: ○57 (Tick as appropriate)	SDigital □ Ba		Film no:	
Dial no	Jpeg number*	Description	Scale(s)	View from	Initials/ date	Archive number
1	0001	GENTRAL SITE SUOTS/		VANCOUS	REU	- L
2	0002	conkino shors			04/09/19	
3	0003					
4	0004		1.			
5	0005	` .				
6	0006					
7	0007					
8	0008					
9	0009					
10	0010					
11	0011	<u> </u>				
12	0012	·				
13	0013				_	
14	0014					1
15	0015					
16	-0016					
17	0017					
18	0018					
19	00 19					
20	0000			-		
21	0021					
22	0022	V		4		PLATE 5
23	0023	E FAC NED SEC 101	IXIA	Ė		
24	00 24	+	1	V.		
25	0025	TRIVICATION S	141	5	_	
26	0026	→	4	V		
	0027	1	1	1/		
28	0028	TRIVIENOS IZRON W		U		
29	0029	É FAC REP SEC 102	1×0.5	E	RED	
30	0030	<u> </u>	1x0-5		05/09/19	
31	0031	5176/ Work We SMOIT				
	0032				-	
1	00 93	J		/		y is
		E FAL REP SÉC 102	XIND.5	C		
35	0035					
36	0036	1	1	V/	7	PLATE 1
	ded? □	Comments:				

^{*} Turn dial to 'review' and the jpeg number appears in the top right hand corner



Site Code: 222651/ SOUYAND TOW, HAMP SAIRE

PO/PS:	NOU	Camera no: 0 57 (Tick as appropriate) 🖾 Dig	gital 🗆 B	&W photo	Film no:	2
Dial no	Jpeg number*	Description	Scale(s)	View from	Initials/ date	Archive number
1	0037	SITE/WORLING SHOTS		VANUOS		roof for Arma ca
2	0038	1			05/09/19	1 2 1 3 5
3	0039					
4	0040					
5	0041	+	/	V		
6	0042	EXCAVATED TREVEY 86073 TAI	/	VANOS		
7	0043					
8	0044					
9	0045					
10	0046					alie".
11	0047					
12	0048					\$1.55 \$1.55
13	0049	→	/	V	V-	Par
14	0050	SITE WORKING SHOTS		VARIOUS	REW	
15	0051				10/09/19	
16	0052					
17	0053					
18	0059					
19	0055					
20	0056					
21	0057					***
22	0058					
	0059		/	\forall	4	
	0060	SITE/ WONE INC SMOTS				
	0061					*
	0062			/		Name of the state
27	0063		 	/		
	0064		/-			
	0065					
	0066					
	0067	V	/			
	0068	Service Plans				
	0069				10	
	0070	SITE/ WORKING SHOTS			REW	75
3	0071			-	13/04/19	
36	2500	1			7	
Downloa	ded? □	Comments:				

^{*} Turn dial to 'review' and the jpeg number appears in the top right hand corner

Site Code: 222651/50043 Site Name: MONTEFIONE BOILER HOUSE, SOUTHAMPTOW, HAUTS

ſ			(Tick es				
ļ	PO/PS:	NEV	Camera no: 057/D47 Tappgopriate) ™ Dig	gital □ B&			
	Dial no	Jpeg number*	Description	Scale(s)	View from	Initials/ date	Archive number
-	1	0073	Evoreno Shot	-	- 1 ·	NEW	
	2	0074 K			IEU .	13/09/19	
	3	, , ,	TR 2 FULLY EXCAVATED		\$		Nastrania Partition and an analysis
-	4		TR J FULLY EXCAVATED		4	<u> </u>	
ŀ	5	0077	W FAC NED SEC 72	Ixla	\mathcal{U}		
-	6	0078	1/	1	1		
-	7	0079	oblique vácu tr 3	146	NU .		
<u> </u>	8	0080					
	9	008	TRENCH	1	41	Ec.	
*	⊋ 10	0082		1 m	W	Eq/09/19	
		0033	PLAN SHOT OF THE	1 m	W	1)	
ŀ	12		W FAC. SEC BENT TRENIS	2m	W	51	PLATE 4
	13	6086	EPLAN SHOTOF PERS 5	2 m	W	<i>a</i>)	
	14	0086	WA FAC SEC SES TRENCHS	1 m	V	1,	
L	15	0037	PLAN SHOT OF SEE TRENCH G	1 m	W	l,	
	16	O 88		lm	S	. 1)	
		0089	SFAC. REPSEC TR 7		<u>S</u>	Li	
	18	0090	11 (1)			1)	
L	19	0091	PLANSHOTTR7		W	١٦	
	20	0092	1)	1	E	11	1 A 1
	21		-AVOID				
	22	००१५	WE FAC. BEP. SECTR 8	2 m	SU	tr	
	23	0096	PLAN SHOT OF TRB	1m	W	LI	
	24	0096	W FAC SECT TRIO	2m	W	11	
		0096	()	()	()	11	
			92AN SHOT OF TRIO	Im	N	11	
		8000	1)	()	N),	
	28	0099	(1	(+	(1		
			NFACSEC TR9	2	N.	25/89/19	W. E.
	30	0101	. 11	1	N ·	20/09/19	
	31	0102	PLAN SHOT OF TRA	1	N	2	
	32	0103-12	TKII Working slet	1/	E	24/11	
	33	0143-	7	Im		1	
	34	0145-12	2. Dell Working Set		V	<u>y</u>	
	35	P/M9/01/3	Western Slots in all the		NW	25/4/19	y i j
	36	WATE 3	excaption per concrete rap	f" /	V	1	
	Downloa	ded? □	Comments: 127 = FRONT COVER				

^{*} Turn dial to 'review' and the jpeg number appears in the top right hand corner

Site Code: 222651/1843 Site Name: MONTOFICE BOILER HOUSE, SOTON

PO/PS:		Camera no: 655 (Tick as appropriate) □ Di	igital □ B&	&W photo	Film no:	
Dial no	Jpeg number*	Description	Scale(s)	View from	Initials/ date	Archive number
1	134	TR 12 (FOUNDTIONS) VIBLIFROM & COMBRAL SITE SHOTS	0.5	62	27.9.19	11. 13. 23.
2	135	b	0.5+2.0	b	1 1	🥫 ــــــــــــــــــــــــــــــــــــ
3	138	CEMBRAL SITE SHOTS			30/67/19	100
4	1					
5	14)					
6	142	EVALUE TO STOKE AMMAGE		3		
7	-143			\		1604. 182
8	144					
9	145					
10	196			ļ		90
11	147					
12	14 8					
13	149					6.1
14	150			-		
15	15 1			SM		ar û Gwe
16	152			NV.		
17	153			لهاء		
18	154					(Diens
19	155					
20	15 L					\$ 14 m
21	157					gjaji zarp
22	15 4					
23	15.9					
24	160			-		
25	19)					
26	162		سلد	<u></u>		
27	163	N FADRA REL SEC OF ROLLING	22	7)		
28	164	11 11	15	4		
29	165	FIMTHED PO-LINUS		E		
30	161			SE		
31	167	S FAC SEL OL HOSPING SHOW RED, NAK.	IM	S	L	PLATE 3
32						25
33	-	41.40				
34					<u> </u>	
35						
36) Y
Downloa	ded? □	Comments:				

^{*} Turn dial to 'review' and the jpeg number appears in the top right hand corner
